


Current Works



Key construction milestones



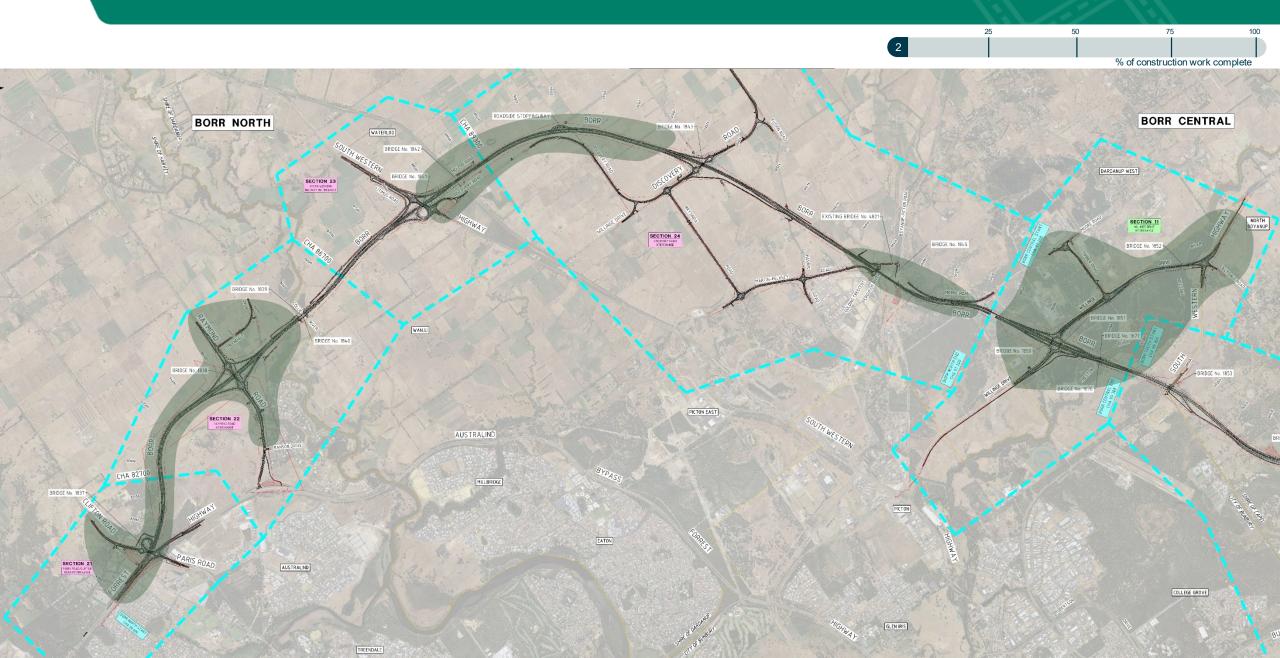







Willinge Drive | S11:

- Continued to import sand for embankment areas
- Construction of access tracks and power pole pads
- Temporary diversion works

Paris/Clifton | S21:

 Commenced import sand and service diversion bund embankment construction

Raymond/Treendale | S22:

- Continued to import sand for embankment
- Commenced import of rock fill for embankment foundation treatment

Waterloo | S23:

- Test pitting completed to validate topsoil thicknesses and foundation treatments
- Drainage slots cut to drain perched water
- Site compound establishment started

Boyanup/Picton | S24:

- Boyanup Picton Road go line and stockpile area established
- Topsoil stripping commenced for the southern approach to 1845 bridge

Local Procurement Achievements (to 30 September 2021)

Category	Spent to 30/9/21	Committed	% of spend target committed	Number of businesses
South West Business	\$27.5m	\$34.9m	12%	136
Aboriginal Business	\$2.3m	\$4.4m	22%	10



Procurement to end September



4 packages awarded

Rock fill material

Demolition

Wet hire plant

Site wide materials testing



Waiting to award

Fencing
Drainage
Survey
Site offices
Earth works packages x 3
Reinforcement
Concrete
Water Infrastructure
Cleaning
Quarry Products
Runnymede Pit
The Wedge

Quarry products



90-day Upcoming tenders

Mentoring
Agricultural fencing
Temporary diversion works
Local Roads package
Concrete Barriers
Waste management
Piling

3 month – tender lookahead

Package Description	Details	Indicative value	Package Owner	
Local Roads Major Earthworks Package	Section 24 - Local Roads Earthworks - Waterloo/Wireless/Martin P *to be split into 2 or more packages	Extra large (likely Medium)	Jon Bowler	
Agricultural Fencing	S11, 21-24 Agricultural fencing	Large	Luke Senior	
Concrete Safety Barriers	Supply and install concrete safety barriers to Sections 21, 22, 23, 2	Medium	Luke Senior	
Earthworks for temporary diversion	Temporary Diversion Works Forrest Highway - Stage 1 - Section 2	Medium	Damien O'Loughlin	
Waste Management - Site Wide	Scrap Metal Recycling for Structures (SIMS), General Waste, Septic	Medium	Tim Williamson	
Bearings HP Pot	HP Pot Bearings Superstructure Package	Small	Shane Gallagher	
Heavy Cranage	Heavy T-Roffs Lifts Craneage Package - bridges 1850, 1851, 1852,	Small	Shane Gallagher	
Heavy T-Roffs Transport	Heavy T-Roffs Transport for site storage - erection delivery (PCY - T-Roffs) from site storage to erection place (Intersite movement)	Small	Shane Gallagher	
Elastomeric Bearings	Elastomeric Bearings Superstructure Package BR 1677	Small	Shane Gallagher	
Expansion Joints	Expansion Joints Superstructure Package	Small	Shane Gallagher	
Drainage around MSE Walls	MSE Drainage Substructure Package (TBC)	Small	Simon Blazejczyk	
Minor Concrete Precast Items	Minor Concrete Precast Items for bridge works (BR 1850&51, 1852	Small	Mitch Jones	
Bored Piles North Section 23	Bridge Piling Foundations 1842 plus CMC Columns for BR 1841&1	Small	Mitch Jones	
Plant Hire	Site Wide - Wet Hire and possibly Dry Hire	Small		
Mentoring	Mentoring as extension of Yaka Dandjoo project (panel contract)		Small	Damien Chalk
Hydromulching Services	Site wide	Legend Small <\$500k Medium <\$2.0M Large <10.0M	ТВС	Jon Bowler
Septic Tank Installation - TBC	Septic Tank Installation - TBC		ТВС	Simon Blazejczyk

Extra Large

>\$10.0M

Working with SWGA | Delivery Strategy

Wet + Dry Hire



- Rates based
- Short-long term agreement
- Lower value

Subcontract



- Package of work
- Various scopes / values
- Requires contract / project management

Feedback from market

Packages too **Large**



SWGA ACTIONS

Industry Focus Group to determine pain points and right-size opportunities.


Local Content Advisor (Scott Radici) to discuss your target / preferred opportunities. Not **Core** Business




Contract conditions



MAIN ROADS WESTERN AUSTRALIA





YAKA DANDJOO PROGRAM PHASES

