



Australian Government

BUILDING AUSTRALIA




mainroads
WESTERN AUSTRALIA

Construction Update

June 2026

Toodyay Road construction ramps up

Construction activity on the Toodyay Road Upgrade project is continuing, with earthworks and clearing on the eastern sections of the alignment between Dryandra Road and Jingaling Brook Road making good progress. In June, works will get underway in the section of the project between Lovers Lane and Clackline-Toodyay Road.

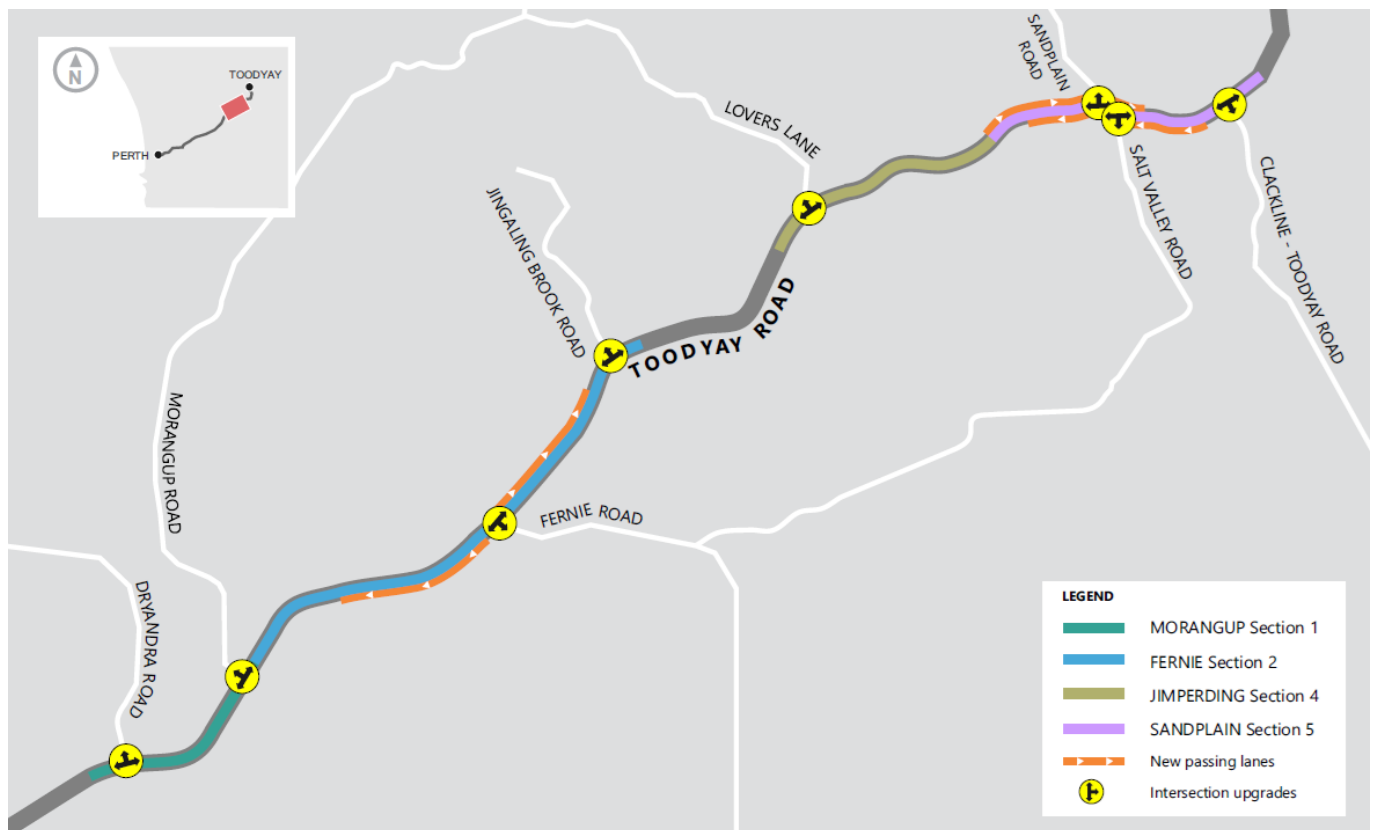

Works overview

Section 1 – Dryandra Road to Morangup Road

Vegetation clearing is underway Section 1, between Dryandra and Morangup Roads, along both sides of Toodyay Road. Clearing in this location will take approximately four weeks to complete.

Section 2 – Morangup Road to Jingaling Brook Road

Earthworks

Earthworks are underway in Section 2, which are required to construct temporary pavement between Morangup Road and Fernie Road, heading towards Toodyay. This temporary pavement will keep traffic flowing on Toodyay Road whilst the permanent upgrades are being constructed. Current works involve

topsoil stripping, embankment construction, importing fill and compaction, along with the application of temporary sealant.

Vegetation clearing between Fernie Road and Jingaling Brook Road is substantively complete.

Temporary traffic realignments

Between Morangup Road and Fernie Road, there will be minor traffic realignments starting in June. As works progress and the temporary pavement is constructed in stages, traffic heading towards Toodyay will be moved onto this new alignment. Once traffic has switched onto the temporary pavement, the construction team can then safely construct the permanent upgrade works on the other side of the road.

Sections 4 and 5 – Lovers Lane to Clackline-Toodyay Road

Vegetation clearing will begin in Sections 4 and 5 in late May, along both sides of Toodyay Road. As these sections include the realignment of Toodyay Road, some clearing will also take place away from the current road. Clearing in this location will take approximately 12 weeks to complete.

We understand that vegetation clearing is a key concern for many in the community, and we are committed to managing this work carefully and responsibly. Clearing will be kept to what is essential to complete the project safely and efficiently.

Before we undertake clearing, our team walk the project alignment with contractor NRW to identify opportunities to prune vegetation instead of removing trees wherever possible. We are also donating suitable branches to cockatoo rehabilitation centres, offering timber to local woodworkers and repurposing mulch for landscaping.

For more information on the environmental management considerations around the Toodyay Road Upgrade project, please view our Community and Environment Fact Sheet on the project webpage.

Bridge construction

Construction of the new Jimperding Brook Bridge is well underway. Clearing in this area has been completed, and we have installed 16 bored piles, which will become the foundation of the bridge. The next stage of works in this location will include construction of pile caps, piers and abutments.

The bridge is being built 60 metres north of the current Toodyay Road alignment in pastoral land.

Traffic management

Traffic management will be in place in various locations as construction progresses along Toodyay Road. Please pay attention to signage and be aware of changing traffic conditions including realignments and temporary speed limits.

We thank road users for their patience and ask everyone to drive with care and courtesy while these essential works are underway.

Further information

The Toodyay Road Upgrade will significantly improve safety and efficiency along the Wheatbelt section of Toodyay Road.

To find out more about the project, please visit our project webpage where you can sign up for project updates [Toodyay Road Upgrades | Main Roads Western Australia](#) or contact us on 138 138 or at enquiries@mainroads.wa.gov.au for project information.
